


Quarterly Project Status Report | **DEC 2020**

THE PANTHER ISLAND/ CENTRAL CITY FLOOD PROJECT

Quarterly Update



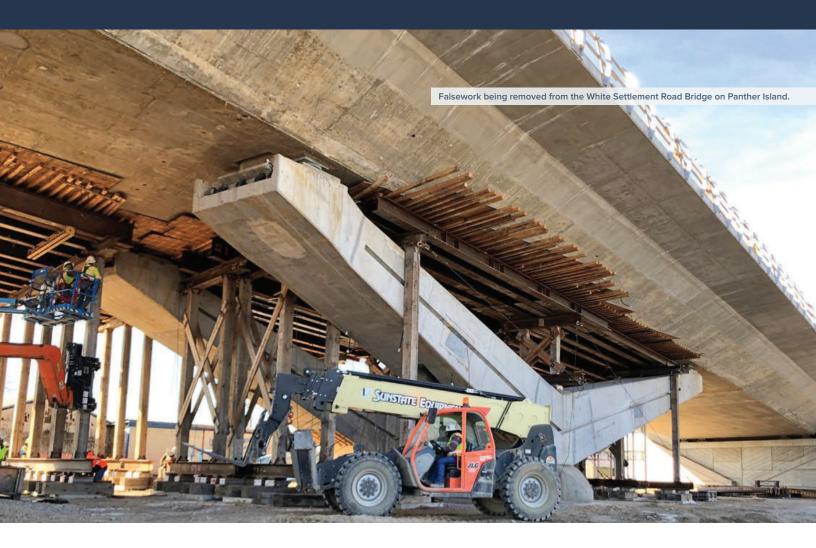


PANTHER ISLAND/CENTRAL CITY FLOOD PROJECT

The Panther Island/Central City Flood Project is a multi-agency collaboration between the Tarrant Regional Water District, US Army Corps of Engineers, the City of Fort Worth and Tarrant County. The project was started in 2004 and expanded in 2009 (adding the Gateway Park flood water retention and recreation corridor). The key component is a 1.5-mile-long rerouting of the river just north of the Tarrant County Courthouse. When completed, the Panther Island/Central City Flood Project will deliver flood protection, environmental clean up of the Trinity River corridor, and recreation for more than 3,000 acres of Tarrant County land.


PROJECT FUNDING SPLIT WITH TRWD BOND OPTION


FUNDING	ESTIMATE	RECEIVED	PERCENT PARTICIPATION	
Local	\$102,000,000	\$102,000,000 100.00%		9%
TIF	\$233,044,000	\$233,044,000	\$233,044,000 100.00%	
TRWD Bonds*	\$247,739,606	\$0	\$0 0.00%	
Federal/State Matching Funds	\$585,826,817	\$116,046,335	19.81%	50%
TOTAL	\$1,168,610,423	\$451,090,335	38.60%	100%

* Bonds issued and guaranteed by TRWD with debt service paid by TIF revenues.



-	E COMPLETION WITH BOND OPTION	ESTIMATE	% OF PROJECT COMPLETE	COMPLETION DATE	
Phase 1 See graphs on p.3	Project Design, Relocation, Environmental Remediation of the Trinity River Corridor, Demo, Land Acquisition and Utilities	\$394 M	64%	2026	See
Phase 2 See graphs on p.3	Three new traffic bridges over rerouted flood control bypass channel (dry-land construction of bridges to save cost)	\$81 M	104%	2021	graphs on p. 3
Phase 3	Construction of floodwater retention, (valley storage) and recreation components along the Trinity River Corridor	\$155 M	38%	2025	
Phase 4	Re-routing of Trinity River for flood control by constructing a new flood control bypass channel and levee system	\$333 M	15%	2025	
Phase 5	Construction of flood gates (3), storm water pump station, and flood management dam	\$205 M	0.32%	2028	
	TOTAL	\$1.16 B			

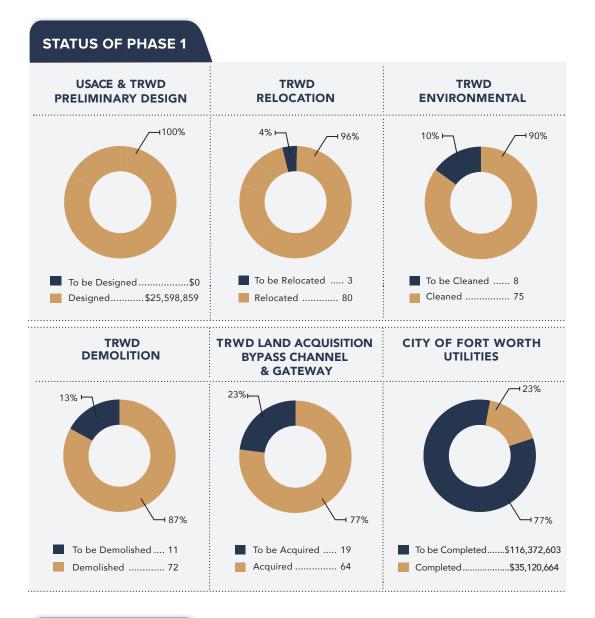

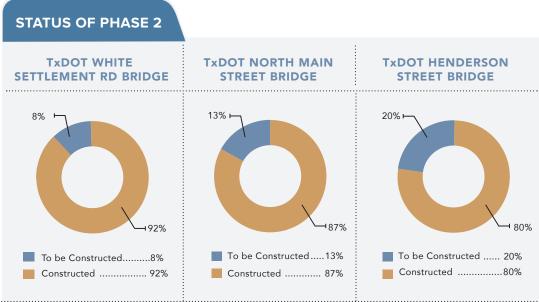

US ARMY CORPS OF ENGINEERS: CENTRAL CITY FLOOD CONTROL PROJECT

TARRANT REGIONAL WATER DISTRICT	2017 ESTIMATE LAND Recategorized	ACTUALS THROUGH DEC 31, 2020	REMAINING
Preliminary Design	\$18,225,972	\$18,225,972	\$0.00
Land Acquisition	68,028,266	63,771,115	4,257,151
Flood Control Cash Match	50,900,362	31,647,074	19,253,288
Relocation	59,790,856	53,658,846	6,132,010
Demolition	15,802,874	6,785,388	9,017,486
Environmental	38,098,850	34,916,990	3,181,860
TRVA Program Coordination	27,197,476	21,068,852	6,128,624
CITY OF FORT WORTH	2017 ESTIMATE LAND RECATEGORIZED	ACTUALS THROUGH DEC 31, 2020	REMAINING
Sewer and Water Relocation	\$71,680,516	\$18,591,816	\$53,088,700
Storm Water Relocation	23,549,203	4,773,574	18,775,629
Franchise Utilities	20,169,474	10,251,722	9,917,752
Local Street Modifications	5,521,441	3,378,791	2,142,650
City of FW Program Management	6,635,424	1,503,551	5,131,873
LOCAL SUBTOTAL	\$405,600,714	\$268,573,691	\$137,027,023

EDI HUD	2017 ESTIMATE LAND Recategorized	ACTUALS THROUGH DEC 31, 2020	REMAINING
Land (Offests Local Above)	\$4,487,035	\$4,485,535	\$1,500
US ARMY CORPS OF ENGINEERS	2017 ESTIMATE LAND RECATEGORIZED	ACTUALS THROUGH DEC 31, 2020	REMAINING
Preliminary Design	\$7,372,888	\$7,372,888	\$0.00
Valley Storage	124,231,564	59,730,302	64,501,262
Ecosystem Restoration	38,551,750	0.00	38,551,750
North Bypass Channel	74,290,882	10,510,296	63,780,586
South Bypass Channel	104,401,759	9,367,370	95,034,389
Flood Gates and Pump System	99,385,763	662,870	98,722,893
Dams and Channel Expansion	85,528,943	0.00	85,528,943
USACE Program Management/Contingency	48,356,327	1,139,538	47,216,789
LOCAL	2017 ESTIMATE LAND RECATEGORIZED	ACTUALS THROUGH DEC 31, 2020	REMAINING
Less Local Flood Cash Match	-\$45,900,363	-\$31,647,074	-\$14,253,289
FEDERAL/STATE SUBTOTAL	\$540,706,548	\$61,621,725	\$479,084,823

TOTAL USACE FLOOD CONTROL PROJECT \$946,307,262 \$330,195,416 \$616,111,84
--

FEDERAL / STATE MATCH

QUARTERLY PROJECT STATUS REPORT

TEXAS DEPT OF TRANSPORTATION: BRIDGES PROJECT

TARRANT REGIONAL WATER DISTRICT	2017 ESTIMATE Land recategorized	ACTUALS THROUGH DEC 31, 2020	REMAINING
Land Acquisition	\$31,006,251	\$28,304,561	\$2,701,690
CITY OF FORT WORTH	2017 ESTIMATE Land recategorized	ACTUALS THROUGH DEC 31, 2020	REMAINING
Bridge Costs Local Share	\$33,973,387	\$33,733,372	\$240,015
City of FW Project Management	0.00	351,970	-351,970
LOCAL SUBTOTAL	\$64,979,638	\$62,389,903	\$2,589,735

TEXAS DEPT OF TRANSPORTATION	2017 ESTIMATE LAND RECATEGORIZED	ACTUALS THROUGH DEC 31, 2020	REMAINING	
Henderson Street Bridge	\$17,598,353	\$19,432,804	- \$1,834,451	
White Settlement Road Bridge	17,792,487	19,194,759	-1,402,272	
North Main Street Bridge	11,414,779	11,565,035	-150,256	
Contingency - Federal	2,801,685	0.00	2,801,685	
FEDERAL/STATE SUBTOTAL	\$49,607,304	\$50,192,598	-\$585,294	

TOTAL TXDOT BRIDGES PROJECT	\$114,586,942	\$112,582,501	\$2,004,441
-----------------------------	---------------	---------------	-------------

LOCAL PROJECTS: WITH OR WITHOUT FLOOD PROJECT

TARRANT REGIONAL WATER DISTRICT	2017 ESTIMATE Land Recategorized	ACTUALS THROUGH DEC 31, 2020	REMAINING
Marine Creek/Stockyards Connection	\$10,245,376	\$0.00	\$10,245,376
Bypass Local Share (Hardscape/Softscape)	21,834,669	3,507,109	18,327,560
TRVA Program Coordination	3,100,000 0.00		3,100,000
CITY OF FORT WORTH	2017 ESTIMATE LAND RECATEGORIZED	ACTUALS THROUGH DEC 31, 2020	REMAINING
Panther Island Sewer and Water	\$15,827,650	\$0.00	\$15,827,650
Panther Island Storm Drainage	13,631,000	0.00	13,631,000
Gateway Park	6,668,614	0.00	6,668,614
TOTAL LOCAL PROJECTS	\$71,307,309	\$3,507,109	\$67,800,200

LOCAL CONTINGENCY

TARRANT REGIONAL WATER DISTRICT	NEW ESTIMATE	ACTUALS THROUGH DEC 31, 2020	REMAINING
Budgeted Contingency	\$36,408,910		
TRVA Programmatic Review		\$466,222	
Bond Issuance Costs		690,917	
Debt Service Cost		6,735	


TOTAL CONT	TINGENCY	\$36,408,910	\$1,163,874	\$35,245,036

LOCAL

PROJECT SCHEDULE

PROJECT COMPONENTS	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028
Land Acquisition Bypass Channel											
Land Acquisition Gateway Valley Storage		 							1 1 1	- 	
Utilities Sanitary Sewer And Water		1 1 1 1			I I					 	
Utilities Storm Drainage System		1 1 1 1		1		I			1 1 1 1	1 1 1 1	
Bridge Completion White Settlement		1 1 1							1 1 1	 	
Bridge Completion Main Street		1 1 1 1							1 1 1		
Bridge Completion Henderson									1 1 1 1	 	
Bypass Channel North Design & Construction		1 1 1 1							1 1 1	 	
Bypass Channel South Design & Construction		1 1 1 1							1 1 1 1	 	
Valley Storage Gateway		1 1 1 1							1 1 1 1	1 1 1 1	1 1 1 1 1 1 1 1
Valley Storage Rockwood Park/ University		1 1 1 1		1	 				1	1 1 1 1	1 1 1 1 1 1 1 1 1 1
Gates (3)		1 1 1 1							1 1 1		
Dam & Locks		1 1 1 1		- 					1 1 1		
Town Lake		1 1 1 1								1 1 1 1	
	2018	2019	2020	2021	2022	2023	2024	2025	2026	2027	2028



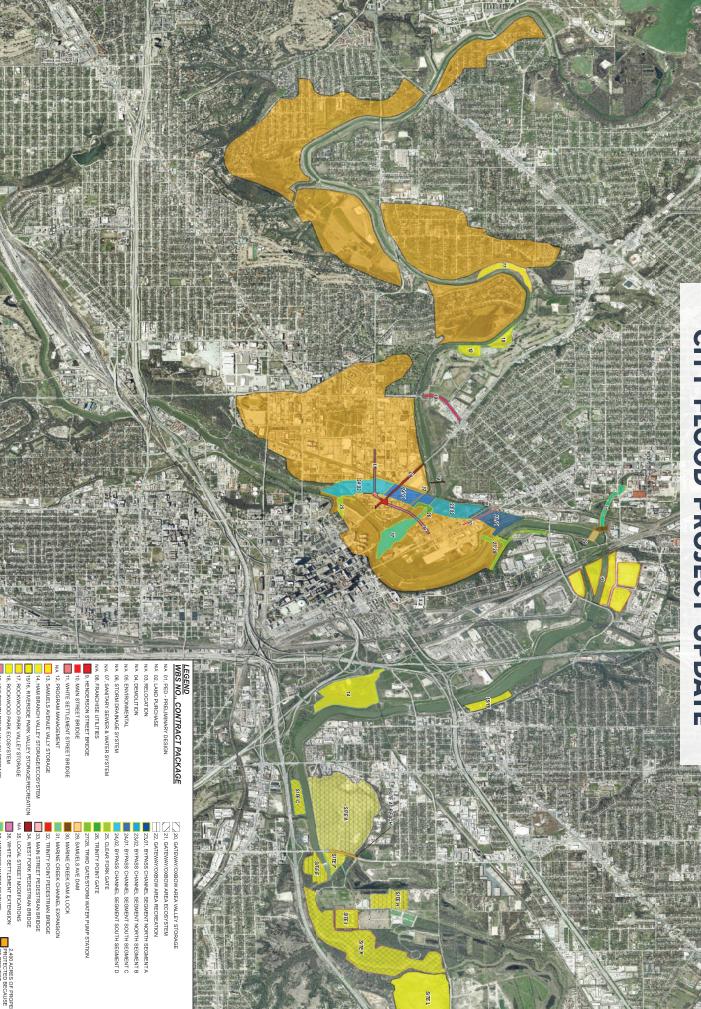

DRIVE VALLEY STORAG

37, INTERIOR WATER FEATURE
